


BBS Planning

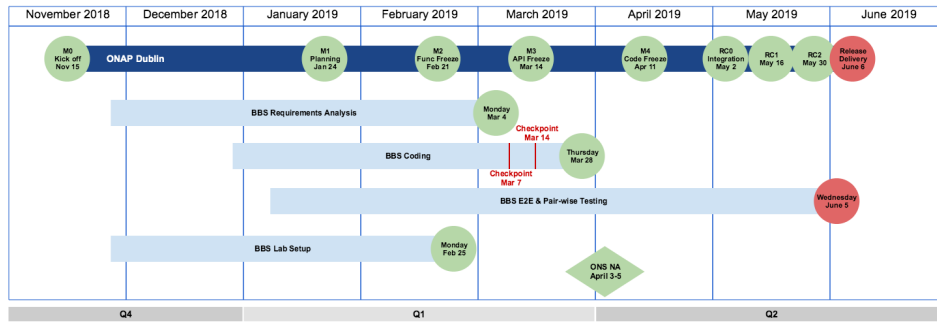

	Task	Start	End	Status
1	Requirement Analysis			
1.1	Finalize BBS architecture	Mon 11.26.18	Tue 12.11.18	COMPLETED
1.2	Building Team	Mon 11.26.18	Wed 12.05.18	COMPLETED
1.3	Create Epics In Community JIRA	Tue 12.11.18	Fri 12.21.18	COMPLETED
1.4	Create user stories In Community JIRA	Fri 12.21.18	Tue 12.25.18	COMPLETED
1.5	Make Workloads, Acceptance criteria, Plan, Dependencies	Tue 12.25.18	Mon 1.07.19	COMPLETED
1.6	Low Level Design (Output specification for project design to review) 1. LLD for SDN-C & Access SDN M&C 2. LLD for SDN-C & Edge SDN M&C 3. LLD for VES Event definition 4. LLD for topology discovery from SDN M&C 5. LLD for External API 6. LLD for PRH enhancement	Mon 1.07.19	Mon 1.14.19	COMPLETED
1.7	Low Level Design review	Mon 1.14.19	Thu 1.17.19	
1.8	Model freeze	Mon 11.26.18	Tue 12.11.18	COMPLETED
1.9	Model review	Tue 12.11.18	Tue 12.18.18	COMPLETED
1.10	Model pushed to the community	Thu 1.24.19	Tue 2.05.19	
1.11	API freeze	Tue 12.18.18	Tue 12.25.18	COMPLETED
1.12	API review	Tue 12.18.18	Tue 12.25.18	
1.13	API pushed to the community	Thu 1.24.19	Mon 3.04.19	
2	Coding			
2.1	Code Checkpoint 1		Thu 3.07.19	
2.2	Code Checkpoint 2		Thu 3.14.19	
2.3	Code freeze	Tue 12.25.18	Mon 3.18.19	
2.4	Weekly Code review	Tue 12.25.18	Fri 2.08.19	
2.5	Unit test	Tue 12.25.18	Fri 2.08.19	
2.6	Code pushed to the community	Tue 12.25.18	Thu 3.28.19	
3	Testing			
3.1	E2E Test design and demo strategy	Mon 1.07.19	Wed 1.16.19	COMPLETED
3.2	E2E Test design and demo strategy review	Wed 1.16.19	Fri 1.18.19	COMPLETED
3.3	Internal Demo review	Mon 1.07.19	Tue 3.12.19	
3.4	Develop test plan	Fri 2.08.19	Tue 2.12.19	COMPLETED
3.5	Project Test case output	Fri 2.08.19	Tue 2.12.19	

3.6	Project Interface self test	Fri 2.08.19	Wed 2.27.19	
3.7	Integration test plan	Fri 1.18.19	Fri 1.25.19	COMPLETED
3.8	Integration Test case output	Fri 1.25.19	Sat 1.26.19	
3.9	Integration test	Fri 2.08.19	Sat 3.09.19	IN PROGRESS
3.10	Internal Demo Show Round1	Mon 3.11.19	Thu 3.14.19	
3.11	Internal Demo Show Round2	Mon 3.18.19	Thu 3.21.19	
4	Lab Setup			COMPLETED
4.1	Development Environment (CI/CD, Code repo)	Mon 11.26.18	Fri 12.07.18	COMPLETED
4.2	Development Environment (local env, local test env)	Mon 11.26.18	Fri 12.07.18	COMPLETED
4.3	Detailed lab topology (wiring diagram)	Wed 12.26.18	Wed 1.09.19	COMPLETED
4.4	Detailed lab topology (wiring diagram) review	Wed 1.09.19	Wed 1.09.19	COMPLETED
4.5	Material ready	Wed 12.26.18	Wed 1.09.19	COMPLETED
4.6	Demo Lab setup	Fri 2.01.19	Mon 2.25.19	COMPLETED
