


Release Planning: Guilin

[blocked URL](#)

Release Schedule r4

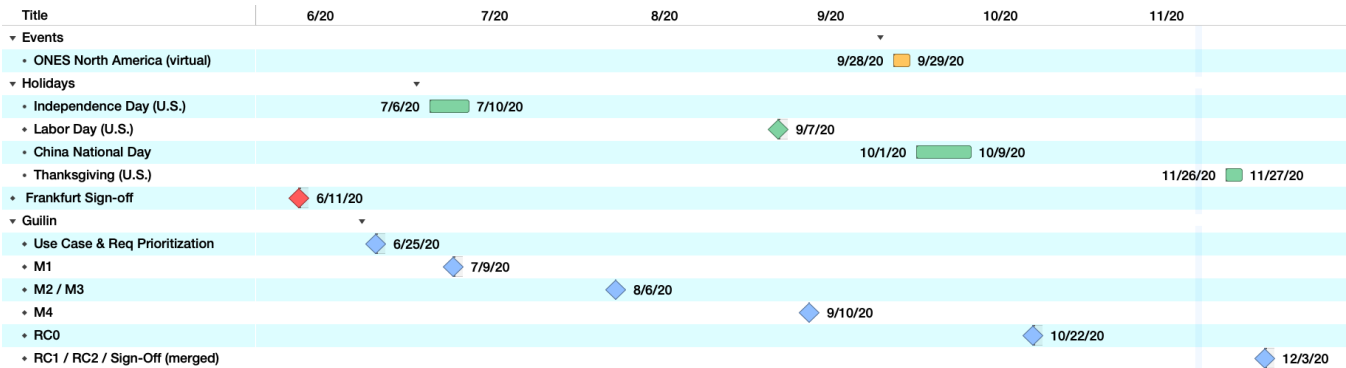

Change Log

Date	Event or Update	Milestones Affected
June 24	Initial version of schedule approved by TSC by mail vote .	N/A
July 9	M1 milestone requirements not met. TSC agrees to slip M1 to July 13.	M1
July 13	M1 milestone requirements not met. M1 slips to July 16.	M1
July 16	Project milestone status 100%, but requirements still not resolved. M1 slips to July 23.	M1
July 23	TSC approved M1 (2 week slip from original plan)	M1
August 6	M2/3 milestone requirements not met. M2/3 slips to August 11	M2/3
August 13	TSC approved M2/3 with conditions	M2/3
September 10	TSC agrees that M4 milestone requirements not met. Agrees to review again on Sept 17.	M4
September 17	TSC approves M4 with exceptions	M4
September 18	Propose moving RC0 to Oct 12, and remaining milestones move out by 1 week (sign off, Nov 12).	RC0, RC1, RC2, Sign-off
September 24	TSC approved moving RC0 to Oct 12, and remaining milestones out by 1 week	RC0, RC1, RC2, Sign-off
October 12	RC0 requirements not met	RC0
October 19	RC0 requirements not met	RC0
October 22	Proposal: Move RC1 to Nov 5 Move RC2 to Nov 19 and combine with Sign-Off	RC1, RC2, Sign-Off
October 22	RC0 approved with caveat that war room continue to resolve SO/OOM issues	RC0
October 22	Schedule proposal approved	RC1, RC2, Sign-Off
November 12	TSC approved merging RC1 with RC2 and sign-off on Nov 19	RC1, RC2, Sign-Off
November 19	RC1 / RC2 / Sign Off moved to Dec 3	RC1, RC2, Sign-Off
