

SO Weekly Meeting 2020-12-02

Agenda Topics:

Project Status in Guilin Release

Guilin Milestone Status

Guilin Impact View per Component

Guilin Release Requirements

Guilin release - non-functional requirements proposed list

New:

Guilin Exception Request for SO

Service Orchestrator Guilin Release M4

RC2 Criteria

Key	Summary	T	Created	Updated	Due	Assignee	Reporter	P	Status	Resolution
SO-3334	Review license scan issues	✓	Oct 22, 2020	Nov 04, 2020		Unassigned	None	=	CLOSED	Done
SO-3332	JIRA Cleanup	✓	Oct 22, 2020	Nov 18, 2020		Unassigned	None	=	CLOSED	Done
SO-3333	Verify readiness of release artifacts	✓	Oct 22, 2020	Nov 18, 2020		Unassigned	None	=	CLOSED	Done

3 issues

Blocking issues :

Key	Summary	T	Created	Updated	Due	Assignee	Reporter	P	Status	Resolution
SO-4116	Cannot Instantiate Volume Attachment Included OpenStack Heat Template VNF	⬮	Sep 07, 2023	Sep 27, 2023		Unassigned	None	⬆	DELIVERED	Unresolved
SO-4109	SDNC calls fail with the new ODL version (chlorine)	⬮	Jun 01, 2023	Jun 29, 2023		Andreas Geissler	Andreas Geissler	⬆	DELIVERED	Unresolved
SO-3783	Error during Deallocate Core NSSI Flow	⬮	Oct 11, 2021	Oct 12, 2021		Unassigned	None	⬆	SUBMITTED	Unresolved
SO-3760	Wrong additional parameter for OOF's terminateNxiRequest	⬮	Sep 05, 2021	Oct 12, 2021		Unassigned	None	⬆	SUBMITTED	Done
SO-4123	SO Development setup fails due to R_CloudConfigMigration Flyway Migration	⬮	Jan 11, 2024	Feb 05, 2024		Unassigned	None	⬆	OPEN	Unresolved

5 issues

License scan issues:

✓ [SO-3292](#) - Issue with the license scan on the JBoss lib used in SO CLOSED


<https://gerrit.onap.org/r/c/oom/+111328>

🔴 [SO-3243](#) - SO-bpmn-infra Container after Java 11 upgrade encountering SunCertPathBuilder Exception: unable to find valid certification path to requested target in CSIT CLOSED

SO committer promotion:

[Service Orchestrator](#)

Way forward for Honolulu:

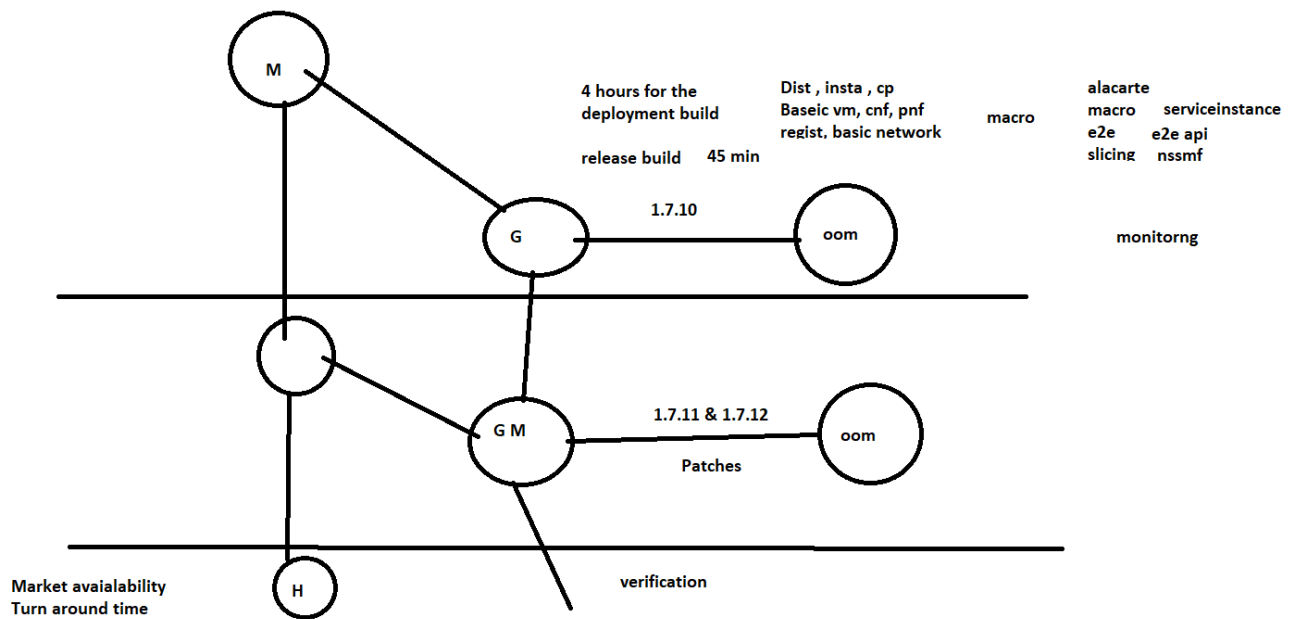

What went wrong:

1. Communication with OOM was not effective
2. OOM delays impacted SO feature delivery delays
3. • Master branch was not stable because a lot of features and Java 11 upgrade and certificate issues
4. • Some testing required additional OOM changes
5. • OOM best practices were not broadcasted to the feature teams
6. • Security best practices / guidance came out in the middle/late of development cycle
7. • Image release number changed multiple times during the Guilin release

What was good:

1. The team could come out of the difficult time and meet the target
2. Response time from SO team was really good
3. In the end the issues were fixed a release was fix.

What can be improved:

1. Reduced code fragments (new projects on the gerrit) for build
2. Introduce the gating as part of the jenkins verification process (2 edged sword to deal with, work with the details).
3. Increase in auto verification
4. • OOM best practices / guidance should come earlier and documented
