


Release Planning: Istanbul



Release Schedule

Approved by the TSC on October 21, 2021 (r6)

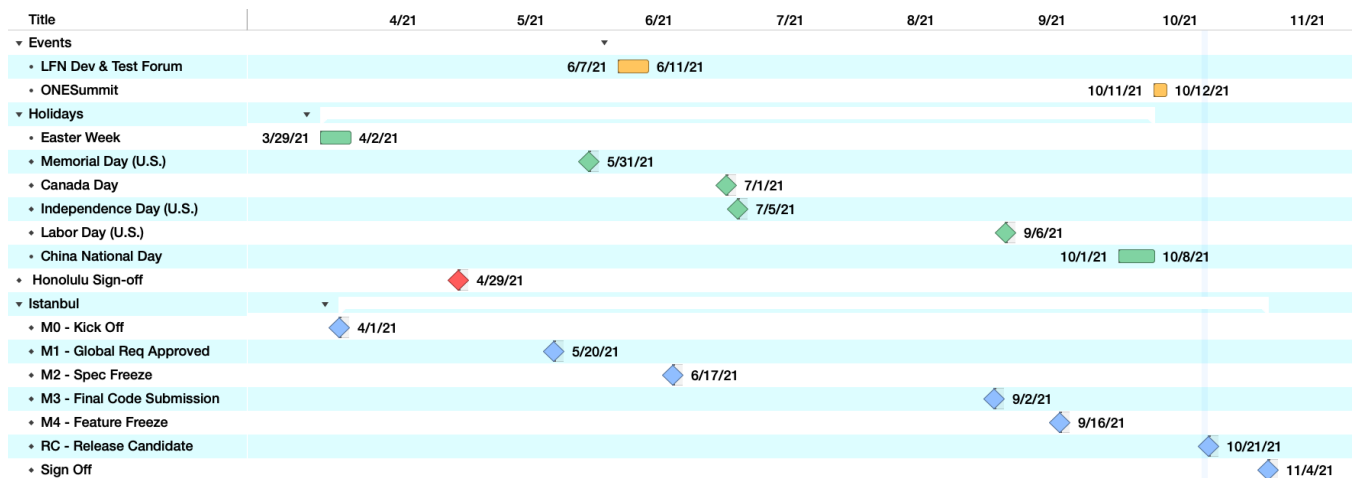

Activity Log

Date	Event or Update	Milestones Affected
Nov 15	Recommended sign off to the TSC. Email vote launched.	Sign Off
Nov 4	The TSC delayed Sign Off to Nov 15. https://wiki.onap.org/x/RZCfBg	Sign Off

Oct 21	The TSC approved RC under the condition that the remaining tasks will be completed by Sign Off. The TSC also approved moving the Sign Off date out one week to Nov 4 (r6).	RC, Sign Off
Oct 18	The TSC agreed that the requirements for RC were not reached. Will review again during the TSC meeting on Oct 21.	RC
Oct 14	The TSC agreed that the requirements for RC were not reached. Will review again during the PTL meeting on Oct 18, followed by an email vote.	RC
Sept 16	TSC approved M4 with conditions .	M4
Sept 9	Remaining M3 items closed	M3
Sept 2	TSC approved M3, conditioned on completion of remaining milestone tasks by M4	M3
Aug 26	TSC approved one week slip to M3. No other milestones affected (r5).	M3
Jun 23	M2 approved by TSC, with exceptions, by email vote .	M2
May 20	M1 approved by TSC, with exceptions. Details here .	M1
May 10	Added ONESummit dates to the schedule (r4) for reference. (No changes to Istanbul release milestones from r3)	None
May 6	Approved by the TSC (r3)	ALL
May 4	New proposal (r3) in response to feedback at May 3 PTL meeting <ul style="list-style-type: none"> Collapsed 3 RCs into a single RC Added more time from M4 to RC Added an additional week between RC and sign off Corrected dates for China National Day holiday. Should be 10/1 -8, instead of 9/27 - 10/1. 	RC0, RC1, RC2
Apr 28	New proposal (r2) in response to feedback from original proposal.	M1 - Sign Off
Mar 18	Proposal presentation to TSC. Requested approval of just the kickoff date of April 1. Other milestones to be discussed at a later date. TSC approved kickoff date ONLY.	M0
Mar 11	Proposal presentation to TSC. TSC expressed concerns about the second half of the release occurring during the summer, which could conflict with summer holidays. Proposal not approved.	ALL
Mar 10	Second draft	<ul style="list-style-type: none"> Added a new milestone before M3 Previous "M3" becomes M4 Added event in June Moved Honolulu sign off to April 8
Mar 4	Initial draft posted	N/A
